


# Progress on Off-site Cleanup Efforts in Japan

# April, 2015 Ministry of the Environment, Japan

# Outline


- Policy Framework
- Progress in Special Decontamination Area
- Progress in Intensive Contamination Survey Area
- Decontamination technology
- New policies announced in Sep 2013
- Efforts to secure Interim Storage Facility
- Public Communication

# Radioactive Pollution Caused by the Accident at TEPCO's Fukushima Dai-ichi NPP

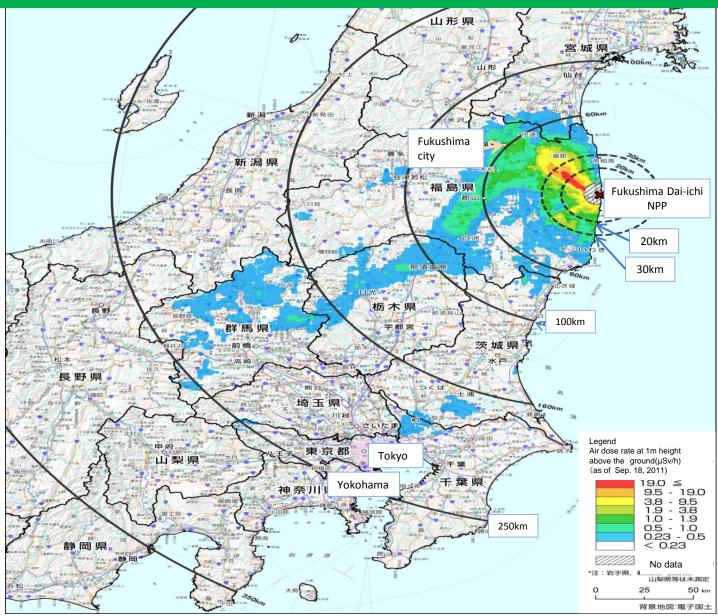

### Radioactive Pollution Caused by the Accident at TEPCO's Fukushima Dai-ichi NPP

Decontamination is one of the measures for radiation protection\*to remove radioactive materials from living environment in order to promptly decrease impacts on human health and living environment. \*The national government aims at a long-term goal to reduce additional annual dose to 1 mSv or less by comprehensive measures for radiation risk management including not only decontamination but also monitoring survey, food safety administration, and health exams .

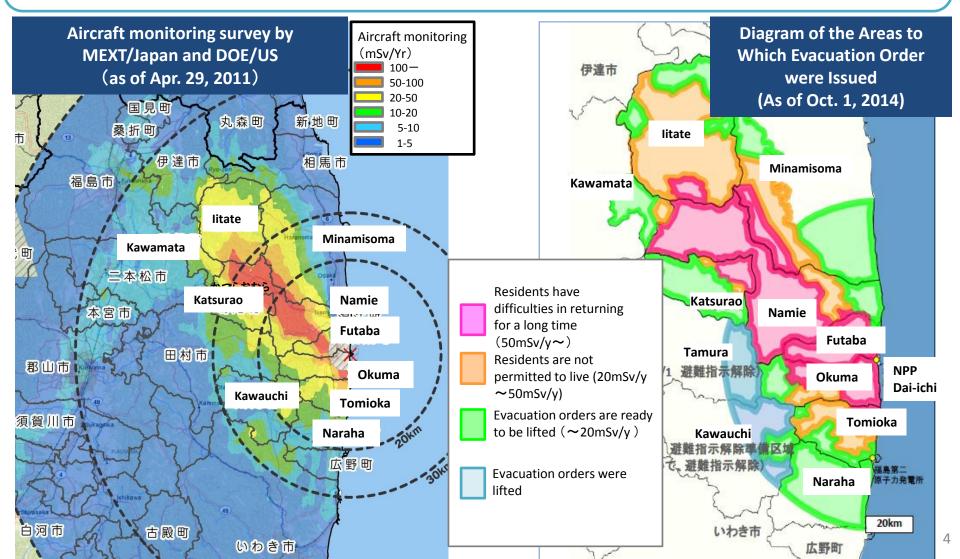

# **Framework of Decontamination**

### **Legislation for Promoting Decontamination**

- The Act on Special Measures Concerning the Handling of Radioactive Pollution came into force on January 1, 2012.
- Based on this Act, the followings are carried out:
  - Planning and implementation of decontamination work
  - Collection, transfer, temporary storage, and final disposal

### **Special Decontamination Area**


- 11 municipalities in (former) restricted zone or planned evacuation zone (<20km from the NPP, or annual cumulative dose is >20mSv)
- Decontamination is implemented by the national government
- (\*) Entire area of Naraha, Tomioka, Okuma, Futaba, Namie, Katsurao, and Iitate. Some area of Tamura, Minami Soma, Kawamata, and Kawauchi.

### **Intensive Contamination Survey Area**

◆ 104 municipalities in 8 prefectures (\*), in which over 0.23 µSv/hour of air dose rate (estimated from the long-term target of annual additional exposure dose, 1 mSv/year, under a certain condition) is observed, were designated.
 ▲ Decontamination is implemented by each municipality. The national

- Decontamination is implemented by each municipality. The national government will take financial and technical measures.
- (\*) Iwate, Miyagi, Fukushima, Ibaraki, Tochigi, Gunma, Saitama, and Chiba

# **Decontamination based on the "Act on Special Measures"**

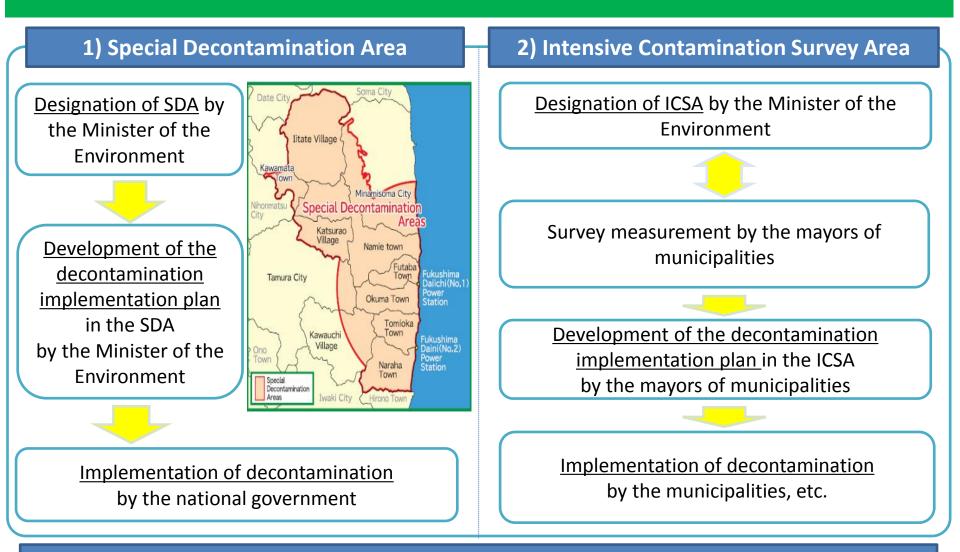

### Decontamination of soil and disposal of generated soil at NPP

Implemented by the nuclear power plant operating company in charge (TEPCO)

# Outline

- Policy Framework
- Progress in Special Decontamination Area
- Progress in Intensive Contamination Survey Area
- Decontamination technology
- New policies announced in Sep 2013
- Efforts to secure Interim Storage Facility
- Public Communication

# Decontamination Policy for the Special Decontamination Area

Decontamination should be implemented taking into account the level of air dose rate

- Area where additional exposure rate is higher than 50mSv/year: MOE conducts demonstration model projects and studies the future demonstration policy based on the lessons learned from the projects.
- Area where additional exposure rate is between 20-50mSv/year: Decontamination is implemented, aiming to reduce exposure dose in residential areas and farmlands to be less than 20mSv/year.
- Area where additional exposure rate is lower than 20mSv/year: Decontamination is implemented for the area as well.
  - MOE reviewed the progress of decontamination in the SDA and announced on September 10, 2013 that it will revise the previous policy that aimed to complete decontamination and transfer generated materials to temporary storage sites in two years (by the end of March 2014) for all municipalities and will promote decontamination in accordance with reconstruction activities depending on the situation of each municipality.
  - MOE announced on December 26, 2013 that it will revise the decontamination plans for Minami-Soma, litate, Kawamata, Katsurao, Namie and Tomioka and set realistic schedules in accordance with the situation of each municipality, in consultation with them.

## Progress in the Special Decontamination Area (1)

Decontamination Plan has been established in all the 11 municipalities, and the progress has been made. Decontamination has been completed in Tamura in June, 2013, and in Naraha / Kawauchi / Okuma in March, 2014.

		Population in Decontamination	Decontamination	Rearrangement of	Progre	ss of the Dec < as of Feb.	ontaminatio 20, 2015 >	n Work	Sche	dule
		Target Area(person) (approx. Figure)	Target Area (ha) (approx. figure)	the Restricted areas, etc.	Decontamination Plan	Temporary Storage Site	Consent of landowners, etc.	Decontamination activities	Residential Areas completed	The rest of other areas completed
ſ	Tamura	400	500	Apr. 2012	Apr. 2012	Secured	Completed	Completed in June. 2013	FY2	013
Whole area	Kawauchi	400	500	Apr. 2012	Apr. 2012	Secured	Completed	Completed in March, 2014	FY2	013
decontamination was completed	Naraha	7,700	2,100	Aug. 2012	Apr. 2012	Secured	completed	Completed in March, 2014	FY2	013
	Okuma	400	400	Dec. 2012	Dec. 2012	Secured	Completed	Completed in March, 2014	FY2	013
Decontamination of residential area was	Katsurao	1,400	1,700	Mar. 2013	Sep. 2012	Secured	Almost completed	In progress	Summer, 2014 (completed)	Within 2015
completed -	Kawamata	1,200	1,600	Aug. 2012	Aug. 2013	approx. 90% Secured	Almost completed	In progress	Summer, 2014 (completed)	Within 2015
	litate	6,000	5,600	Jul. 2012	May 2012	secured	approx. 90%	In progress	Almost completed	Within2016
Decontamination is under operation &	Minami- Soma	13,300	6,100	Apr.2012	Apr.2012	approx. 80% secured	approx.70%	In progress	FY2015	FY2016
in preparation	Namie	18,800	3,300	Apr. 2013	Nov. 2012	approx. 40% Secured	approx. 70%	In progress	FY2015	FY2016
	Tomioka	11,300	2,800	Mar. 2013	Jun. 2013	secured	approx. 90%	In progress	FY2015	FY2016
	Futaba	300	200	May, 2013	Jul. 2014	Under coordination	Under preparation	Under preparation	FY 2	015

Note 1: Necessary areas for securing Temporary Storage Sites might be reviewed in future survey

Note 2: In the municipalities where decontamination was completed, such as Tamura, Kawauchi, Naraha, and Okuma, remaining decontamination shall be implemented for the residents who did not yet consent but newly request decontamination.

# Progress in the Special Decontamination Area (1)

### (as of Mar., 2015)

尹涅			~~~~	< Complet	ted decontamination >
$\sim$	120	A Contraction		Tamura	Whole area decontamination was completed in June, 2013. Evacuation order was lifted on April 1, 2014
	Iitate	mpleted		Kawauchi Naraha Okuma	Whole area decontamination was completed in March, 2014 ※ As for Kawauchi, a part of the evacuation order was lifted on October 1, 2014
-	in residential are Kawamata		Minami- Soma	Katsurao	Decontamination of residential area was completed in July,2014
				Kawamata	Decontamination of residential area was completed in August,2014
本 、	Aug. 2014 Comple in residential are Katsu	earry	Jul. 2014 Completed in residential area	Joban Expressway	Decontamination was completed ※ Reopened between Hirono and Joban-Tomioka on Feb. 22, 2014 ※ Opened between Namie and Minami-Soma on Dec. 6, 2014 ※ Opened between Namie and Joban-Tomioka on Mar. 1, 2015
ſ	April, 2014 Evacuation		Namie	< Schedul	es of decontamination ahead >
ļ	order was lifted	Tamura	Futaba	Kawamata Katsurao	Aiming at the completion of decontamination of remaining areas within 2015
٦	Evacuation order lifted Completed Started	Oct. 1, 2014 A part of Evacuation order area	Okuma Tomioka	litate	Decontamination of residential area was almost completed at the end of Dec., 2014 aiming at the completion of decontamination of remaining area within 2016
F	Ordered Ordered SDA	was lifted Kawauchi	Mar. 2014 Completed in whole area Naraha	Minami- soma Namie Tomioka	Aiming at the completion of decontamination of residential area within FY 2015 and the completion of decontamination of remaining area within FY 2016
	SDA Areas where it is antic face difficulties in retu			Futaba	Aiming at the completion of decontamination within FY 2015 10

# Progress in the Special Decontamination Area 3-1

Progress on decontamination works (executing ratio and ordering ratio) is as follows:

As of Feb. 20, 2015	Tam	nura	Nar	aha	Kawa	auchi	lita	ate	Kawa	mata
< Unit: % >	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio
Residential area	100	100	100	100	100	100	96	100	100	100
Farmland	100	100	100	100	100	100	25	100	18	100
Forest	100	100	100	100	100	100	38	100	56 (54)	100
Road	100	100	100	100	100	100	24	100	4	100

Note 1: Executing ratio is calculated as follows: ①Areas in which decontamination works (weeding, removal of sediment, and cleaning, etc.) are completed / ②Target areas to be decontaminated

Note 2: Ordering ratio is calculated as follows: ③Areas already contracted for decontamination / ②Target areas to be decontaminated Note 3: ①, ②, ③ might be modified with further review

Note 4: The number in () was the number in last month. When there is no change, it is skipped

# **Progress in the Special Decontamination Area 3-2**

As of Feb. 20,	Kats	urao	Okı	ıma	Min So	ami- ma	Tom	ioka	Nai	mie
2015	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio	Executing ratio	Ordering ratio
Residential area	100	100	100	100	7	99.9	17 (14)	100	11	48
Farmland	68 (62)	100	100	100	8 (6)	65	5	100	13	35
Forest	99.9 (99)	100	100	100	34 (31)	79	28 (22)	100	14 (13)	43
Road	32 (23)	100	100	100	2 (1)	65	61 (60)	100	20 (19)	46

Note 1: Executing ratio is calculated as follows: ①Areas in which decontamination works (weeding, removal of sediment, and cleaning, etc.) are completed / ②Target areas to be decontaminated

Note 2: Ordering ratio is calculated as follows: ③Areas already contracted for decontamination / ②Target areas to be decontaminated Note 3: ①, ②, ③ might be modified with further review

Note 4: The number in () was the number in last month. When there is no change, it is skipped

### New Schedule to be Targeted for Special Decontamination Area (1)

- Among 11 municipalities, Decontamination works in Tamura has been completed June, 2013 and the one of in Naraha / Kawauchi / Okuma has been completed in March, 2014
- For Minami-Soma, litate, Kawamata, Katsurao, Namie, and Tomioka, the decontamination plans were revised in Dec. '13 and a realistic schedule that meets the condition of each area were set up in consultation with each municipality and community.
- Decontamination of residential areas and their surroundings will be prioritized for the evacuees to return home.
- The decontamination works of the infrastructure which are important for the evacuees to return home(such as water supply, sewage, and major roads) will be started in advance.
- The decontamination projects should be implemented in an accelerated and smooth manner and the project terms should be shortened as much as possible. The work process should be fully controlled and the progress status should be made open to public.

Minami- Soma	<ul> <li>The residential areas and their surroundings will be decontaminated on a priority basis by the end of March, 2016.</li> <li>The rest will be decontaminated by the end of March, 2017. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible.</li> </ul>
litate	<ul> <li>The residential areas and their surroundings will be decontaminated on a priority basis by the end of March, 2015. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible to be completed by the end of 2014.</li> <li>The rest will be decontaminated by the end of March, 2017. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible to be completed by the end of 2014.</li> </ul>
Note: D	Decontamination work in a municipality is to be implemented based on the premises of formulation of the decontamination plan, securing of temporary storage sites, consent of land owners ,and the ensuring of workers.

## New Schedule to be Targeted for Special Decontamination Area (2)


Kawamata	<ul> <li>The residential areas and their surroundings will be decontaminated on a priority basis by the end of March, 2015. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible to be completed by the end of summer in 2014.</li> <li>The rest will be decontaminated by the end of March 2016. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible to be completed by the end of summer in 2014.</li> </ul>
Katsurao	<ul> <li>The residential areas and their surroundings will be decontaminated on a priority basis by the end of March, 2015. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible to be completed by the end of summer in 2014.</li> <li>The rest will be decontaminated by the end of March, 2016. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible to be completed by the end as much as possible to be completed by the end of summer in 2014.</li> </ul>
Namie	<ul> <li>Areas to be decontaminated, other than the tsunami-devastated areas (Minami-Tanashio, Ukedo-Kita, Ukedo-Minami, Nakahama, Morotake), will be decontaminated on a priority basis by the end of March, 2016.</li> <li>For the tsunami-devastated areas, the residential areas and their surroundings will be decontaminated on a priority basis by the end of March, 2016 by paying attention to the treatment of disaster waste. The rest will be decontaminated by the end of March, 2017. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible.</li> </ul>
Tomioka	<ul> <li>The residential areas and their surroundings will be decontaminated on a priority basis by the end of March, 2016.</li> <li>The rest will be decontaminated by the end of March, 2017. The decontamination will be made in an accelerated and smooth manner and the work term will be shortened as much as possible.</li> </ul>
Futaba	• Decontamination in residential houses and its' vicinity is aimed to be completed within FY 2015.
Note:	Decontamination work in a municipality is to be implemented based on the premises of formulation of the decontamination

plan, securing of temporary storage sites, consent of land owners , and the ensuring of workers.

### The result of Post-Decontamination Monitoring

# OThe dose rate is the averaged value measured in each of the sites. The value immediately after decontamination [green column] is normalizes to be 100%.


Comparison of average figure on air dose rate (assuming the figure after the work as 100)

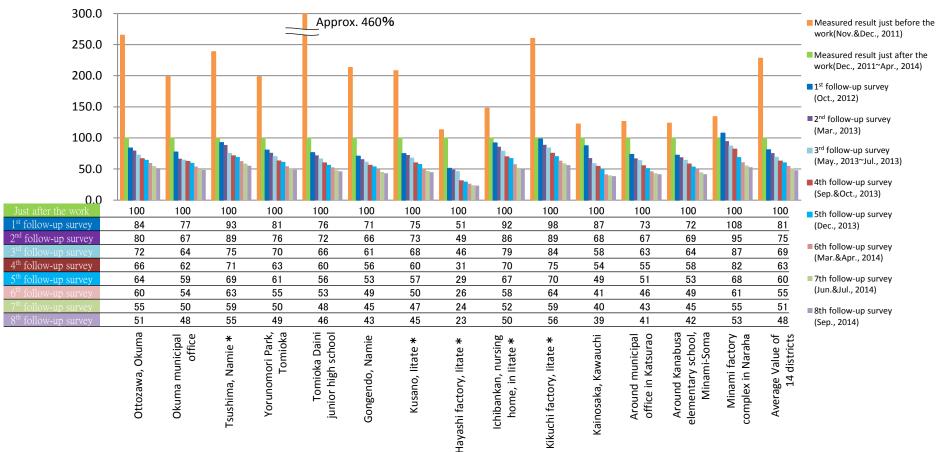

\* : Measurement result just after the decontamination work in Tsushima, Namie and litate, might be possibly low because of accumulated snow Note 1: Measurement figure might be changed by environmental condition, e.g. climate condition, such as rainfall, snowfall, Note 2: It's have passed about one year and nine months from measurement result just after the decontamination work until 5<sup>th</sup> follow-up survey, during that time, the dose rate resulting from radiocaesium, about 30% of reduction is expected by physical attenuation.

# Effects of Decontamination Work in Naraha

Decontamination work decreased radiation dose: e.g. approx. 46% in residential area
 Post-decontamination monitoring confirmed that effects of the whole area decontamination have been maintained and that radiation dose has been continuously decreasing

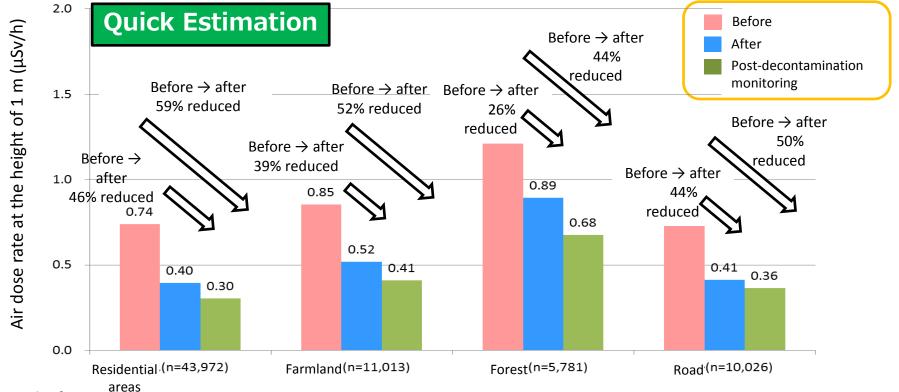

#### Periods of measurement:


Before decontamination: Jun. 2012-Mar. 2014, After decontamination: Jun. 2012-May. 2014, Post-decontamination monitoring: Jul. 2014-Nov. 2014

It is the policy that the whole area decontamination is not to be conducted in principle. However, if post-decontamination monitoring finds hot spots where decontamination effects are not maintained and whose high radiation affects air dose rates of surrounding environment, follow-up decontamination is to be conducted upon each situation, taking into account rationality and feasibility.

# **Overview of the Decontamination Project in Tamura City**

Decontamination work based on the Decontamination Implementation Plan has been finished in Tamura City.

- Work Period : July 5, 2012 ~ June 28, 2013
- Number of Workers : Max. 1,300/day (A total of 120,000 man day)
- Decontamination target area : residential area and a part of forests (area within 20m from the edge) in Furumichi, Miyakoji district
- Volumes of work
  - Buildings 228,249 m<sup>2</sup>(121 family unit)
  - Roads 95.6km
  - Farmland 1,274,021 m<sup>2</sup>
  - Forests 1,921,546 m<sup>2</sup>

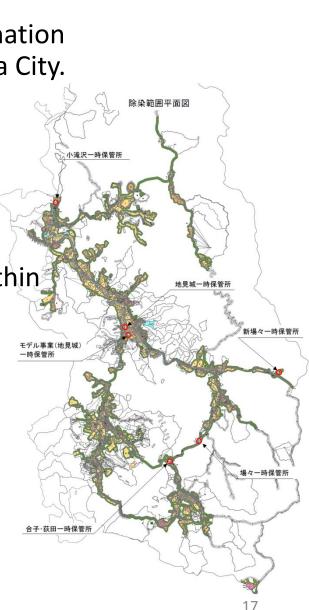

# Lift of Evacuation Order in Tamura City

- April 2012Designated as areas to which evacuation orders are ready to belifted after the Rearrangement of Evacuation Order AreasFormulation of a decontamination implementation plan
- July 2012-Full-scale decontamination workbased on the plan was started
- June 2013- Decontamination work was completed
- Aug.-Nov. 2013- Post-decontamination monitoring



October 2013 Explanatory meeting to local residents


<Reported the result of post-decontamination monitoring of residential houses>


- February 2014-Explanatory meeting to local residents<Set up an inquiry counter and carried out measurement upon residents' requests>
- April 2014 The evacuation order was lifted
  - **Decontamination follow-up** 
    - 1. Consultation counter for decontamination

<Started to measure air dose rate and to check the extent of contamination upon residents' requests>


- 2. Continuous Post-decontamination monitoring
- 3. Removal of contaminated soil depending on the situation

### Effect of Radiation Dose Reduction by Decontamination Work in Tamura City

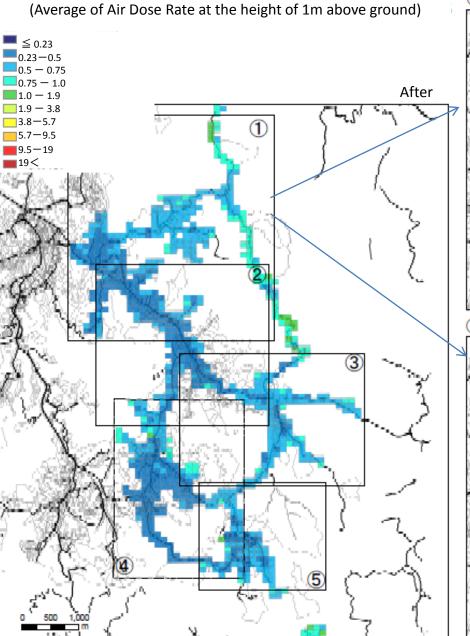

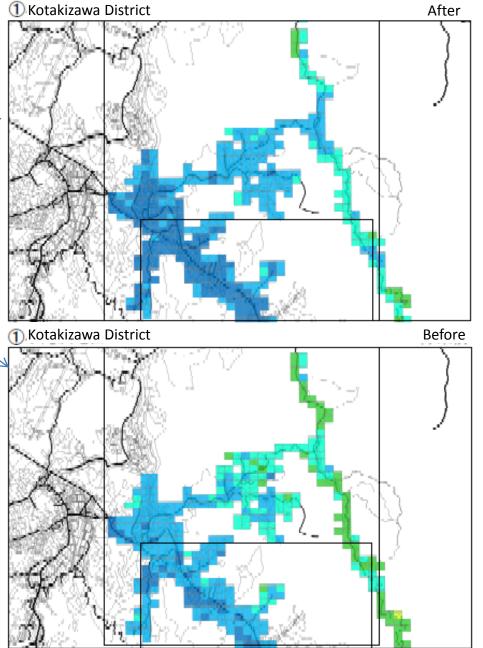

# Before & After the Decontamination Work in Tamura City

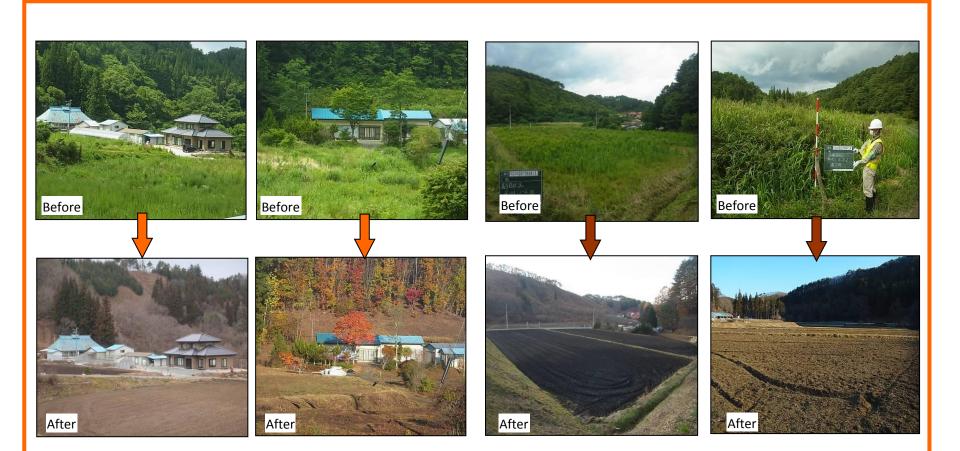

# **Decontamination Activities in Tamura City**



Wiping off rooftop and walls



Wiping off a gutter



High pressure water cleaning of a drain pipe



High pressure water cleaning of paved road




Mowing and removal of sludge



Removal of crushed stones and topsoil, and cover with clean soil


# Effect on Decontamination Work in Tamura City ①

Air Dose Rate 1m above surface

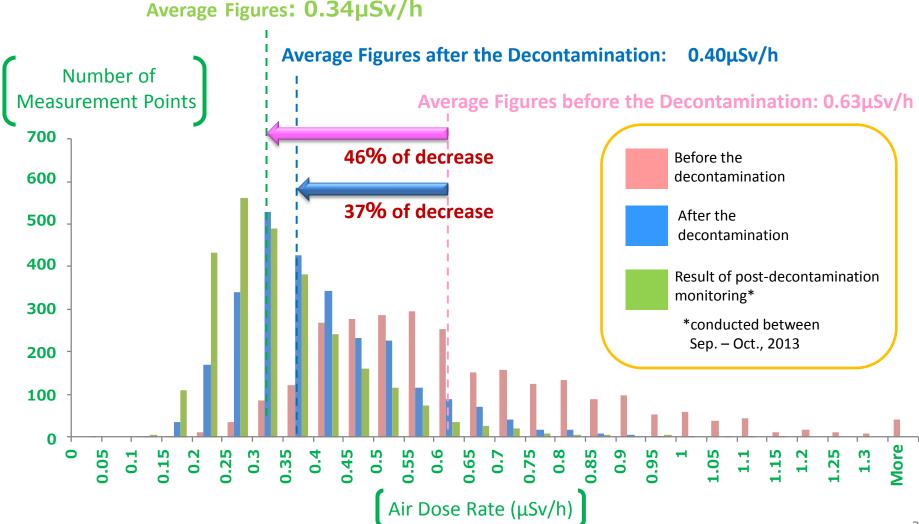

# Effects on Decontamination Work in Tamura City (2)

- Decontamination work has reduced air dose rates.
   e.g. by approx. 36% for residential houses
- The data from the post-decontamination monitoring confirm that the effects of whole area decontamination have been maintained and show that air dose rates have been continuously decreasing.

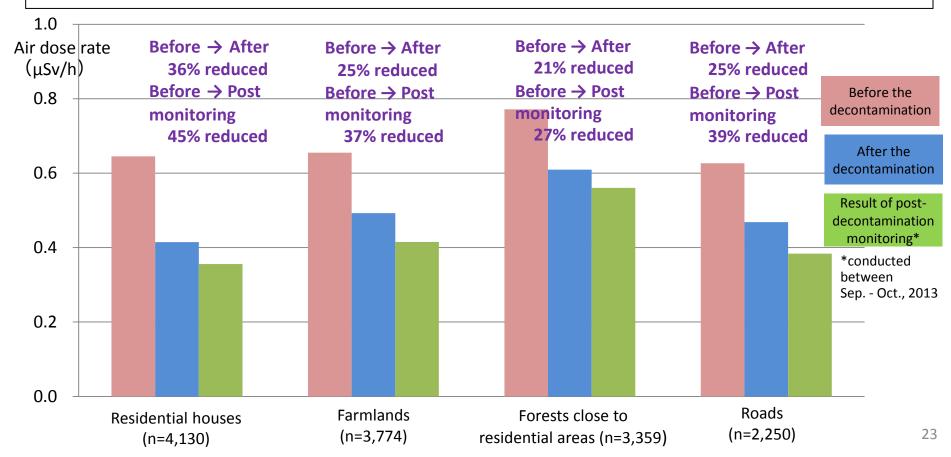

# **Overview of Temporary Storage Site in Tamura City**

- Removed soil has been collected and stored in temporary storage sites.
- Air dose rate at the entrance of the sites shows no difference after removed soil is stored.
- Radioactive materials has never been detected from leachate or groundwater under the sites.

Air Dose Rate just after InstallationLatest (5/27)Amount of Removed soil (m²)Measurement Result of LeachateMeasurement Result of Groundwater	
Kotakizawa 0.36 0.36 4,242 ND ND	新場々一時保育
Jikenjo 0.32 0.38 2,743 ND ND	and the second
Jikenjo (Model Project) 0.38 0.34 2,626 ND ND	A
Shin-Baba 0.60 0.56 7,985 ND ND	場々一時保管所
Baba 0.40 0.45 1,974 ND ND	
Goshi, Ogita 0.39 0.43 12,149 ND ND	3 24

# **Results of decontamination on Joban Expressway**

After the synergistic work of decontamination by MOE and restoration by East Nippon Expressway Company Limited, the air dose rates have been decreased and fallen much below the targets in the "Decontamination Policy".

#### Outline of decontamination

Zones of decontamination on Joban Expressway


Period	Decem	ber, 2012	2 ~ Jun	e, 2013		Legend Yamamoto Legend
Decontamination area	Areas where air dose rates exceeded 3.8 µSv/h (equivalent to 20 mSv/year) on the roads					Areas to which evaluation orders are ready to be lifted Areas in which residents are not permitted to live Areas where it is expected tha
Main Decontamination method	Road so Future Bridge XTop so	urface : H site : We cor (handrai bil remova	ligh pres eding, Se mpactior I safety I of road s	(removing vegetation) ressure water jet washing Soil mixture, Surface ion <b>ty fence)</b> : Wiping out d surface was omitted for the of the main line.		t residents will face difficulties in returning for a long time As of Oct. 1, 2014 Opened on Apr. 8, 2012 L=14.4km Minami-Soma Kashima SA L=14.4km Minami-soma IC
Result of	decontar	nination				on Dec. 6, 2014
Section (as of June,	Target		e air dose ght of one (μSv/h)		Decreasing rate for Oct.2014 to	Under construction area 双章町 Fukushima
2012)	(μSv/h)	Before	After	Oct. 2014	pre- decontamination	to be opened by March, 2016 Re-opened
①3.8 μSv/h< ~≦9.5 μSv/h	≦3.8	4.3	2.8	0.9	79%	on Feb. 22, 2014 L=16.4km ならはPA 所 推業町
②>9.5 μSv/h	≦9.5	15.7	9.9	2.3	85%	Hirono IC 25

# Outline

- Policy Framework
- Progress in Special Decontamination Area
- Progress in Intensive Contamination Survey Area
- Decontamination technology
- New policies announced in Sep 2013
- Efforts to secure Interim Storage Facility
- Public Communication

## Progress in Intensive Contamination Survey Area $oldsymbol{1}$

#### As of the end of January, 2015

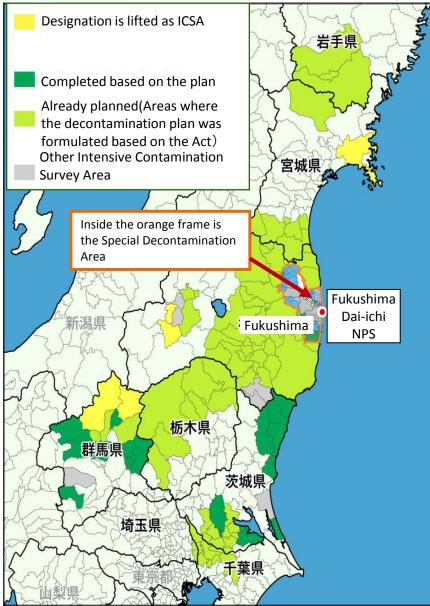

### < In Fukushima prefecture >


- Number of municipalities designated as the Intensive Contamination Survey Area:
  - <u>41 (at the start)  $\rightarrow$  39 (at present)</u>

When the situation becomes different from the required condition of designation, the designation can be lifted. The designation was lifted in two municipalities up to now because of the radiation dose decrease, etc.

- Municipalities that formulated decontamination implementation plans
   (all municipalities that had intended to do):
   <u>36 municipalities</u>
- Municipalities in process of implementing decontamination based on the plans: <u>36 municipalities</u>
- The progress of decontamination (as of the end of February 2015)
   <u>Public facilities: approx. 80%</u>
   <u>Residential houses: approx. 70%</u>
   <u>Roads: approx. 40%</u>
- The end of most of the decontamination plans are set between FY2015- FY2016.

## Progress in Intensive Contamination Survey Area ${f 2}$

#### As of the end of December, 2014

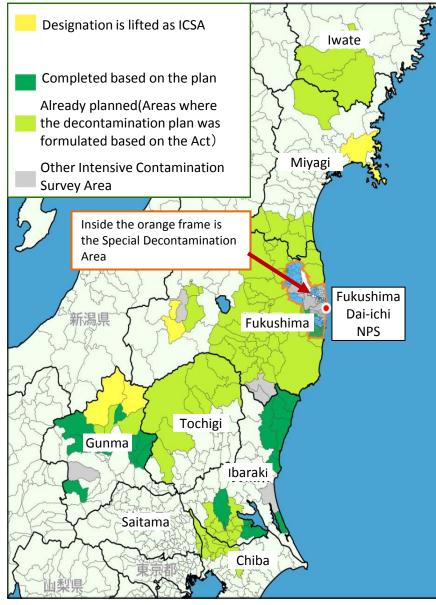

### < Outside Fukushima prefecture >

- ◇ Number of municipalities designated as the Intensive Contamination Survey Area:
   <u>63 (at the start) → 60 (at present)</u>
   When the situation becomes different from the required condition of designation , the designation can be lifted. The designation was lifted in two municipalities up to now because of the radiation dose decrease, etc.
- Municipalities that formulated decontamination implementation plans
   (all municipalities that had intended to do):
   <u>58 municipalities</u>
- ♦ 18 out of 58 municipalities have completed their plans (and continued monitoring of air dose rates).
- $\diamond$ 27 out of 58 municipalities have almost completed.
- The progress of decontamination (as of the end of December 2014)
   <u>Schools & nurseries: almost completed</u>
   <u>Residential houses: approx. 90%</u>
   <u>Roads: approx. 90%</u>

# Progress in Intensive Contamination Survey Area 3

Decontamination implementation plans were formulated in 94municipalities, and progress has been made (in Fukushima: as of the end of Jan. 2015, other prefectures: as of the end of Dec. 2014)

	Number	Municipalities designated as Intensive Contamination Survey Area						
	of	Already	Already formulated the plans					
	municipa lities	decontamination work in progress	Almost completed	Completed	No plan at present			
Fukushima	39	36			3			
Iwate	3	1	2					
Miyagi	8	5	3					
Ibaraki	20	1	7	11	1			
Tochigi	8	4	4					
Gunma	10	1	1	7	1			
Saitama	2		2					
Chiba	9	1	8					
Total	99	49	27	18	5			

# Progress in Intensive Contamination Survey Area 4

Within Fukushima prefecture (As of the end of Feb., 2015)	Ordering Ratio (Number of ordering/Number of planning	Executing Ratio (Number of actual achievement/Number of planning)
Public facilities, etc.	mostly ordered	approx. 80%
Residential houses	mostly ordered	approx. 70%
Roads	approx. 70%	approx. 40%
Farmlands & meadows	mostly ordered	approx. 80%
Forests(in living areas)	approx. 80%	approx. 50%

Note: The table is based on the investigation result conducted by Fukushima prefecture.

The number of planning is the total number until the end of FY2013, which might be increased in future depending on each municipality's status.

Outside Fukushima pref. (As of the end of Dec., 2014)	Ordering Ratio (Number of Ordering/number of planning)	Executing Ratio (Number of actual achievement/number of planning)
Schools and nurseries	ordered	almost completed
Park, Sports facilities	mostly ordered	approx. 90%
Residential houses	mostly ordered	approx. 90%
Other facilities	approx. 90%	approx. 90%
Roads	approx. 90%	approx. 90%
Farmlands & meadows	ordered	almost completed
Forests( in living areas)	mostly ordered	approx.70%

Note: The number of planning is the total number including future plan as of the end of 2014, and might be increased aftertime

## **Result of the review on decontamination in Sep. 2013**

Checkup the status of municipalities tackling leading decontamination and completing decontamination work based on on-going decontamination plan. Effective information shall be shared widely among municipalities in consideration of municipalities' status.

OThe municipalities, implementing leading decontamination work, have been accumulating various original and innovative measures and know-hows, from the view point of the promotion of effective and efficient decontamination work and mutual understanding between local residents.

Example: Excerpted from "Good Practice Collection" (compiled by Fukushima Office for Environmental Restoration, MOE)

<u>Volume reduction of the waste(twigs, etc.)</u>
 <u>discharged from decontamination work</u>
 <u>(in Date city)</u>

Chipping operation in decontamination site



 Cooperation with local residents, delivery of Q &A materials for smooth operation for explanatory meetings (in Fukushima city)



OThere are municipalities of which decontamination work have completed according to the plan as of Jun., 2013



With accelerating and streamlining of decontamination work in consideration of each municipality's status, information shall be shared by updating Good Practice Collection and by guidelines, and also exchanging opinions among municipalities.

# Dissemination of Information regarding Decontamination Progress on the Website

### In case of Fukushima City:

↑ ● 除染についての基礎	青報 ● 除染特別地域の概要・進捗 ● 除	☆ からわせ 除染・放射線 Q&A ♥♥ 酸 熱 傷 範 染実施区域の概要・進捗 ● 除染で取り防 土壌等の管理
<u>- ップページ &gt; 除染実施区域の概要・進捗</u>	世 > 福島県 福島市	•
●除染実施区域の概要・進捗	福島県福島市	
○ 岩手県	除染の進捗状況	
○宮城県	除染実施計画 策定済	
◎ <u>福島県</u>		出典:福島貝除柴対 平成26年6月末
◎ 茨城県	公共施設 [應股数]	住宅同
◎栃木県	計画数 1.482	計画数 65,127
• 群馬県	発注数 1.324 実績数 1.301 (除染実施数: 1301 調査にて終了: 0)	発注数 65.127 実績数 37.601 (除染実施数: 37601 調査にて終了: 0)
○ 埼玉県	道路 [km]	農地:水田 [ha]
◎ 千葉県	計画数 255.1	計画数 2.361.0
	発注数 255.1 実績数 154.8	発注数 2.361.0 実績数 2.361.0
◎ 千葉県		

## For Acceleration of Decontamination and Reconstruction - Interim report of the strategies of the national government and the 4 cities -


### Background

The 4 cities (Fukushima, Koriyama, Soma, Date) requested the national government to accelerate the decontamination and reconstruction and to provide accurate information that could remove public misinterpretation of the target of decontamination.
The national government and the 4 cities developed together an interim report as their

common view of the strategies.

### What the national government could not correctly convey

The long term target of radiation protection is the additional exposure dose of 1 mSv/yr. Decontamination is only one of the radiation protection methods. 1 mSv/yr is not a limit of exposure or a boundary between safety and danger. The government uses the value of air dose rate 0.23  $\mu$ Sv/h as a criterion to specify the Intensive Contamination Survey Area but does not set it as a goal to be achieved only by decontamination activities. 0.23  $\mu$ Sv/h is a numerical value conservatively estimated based on a hypothetical life pattern.



## For Acceleration of Decontamination and Reconstruction (2) - Interim report of the strategies of the national government and the 4 cities -

### New findings

### (1) Air dose rate

Decontamination and radioactive decay over the past three years have decreased air dose rates.

### (2) Individual exposure dose


The level of annual individual additional exposure is about 1 mSv for many residents. Individual additional exposure is approx. 1 mSv/yr for the residents living in the area where the air dose rate is about 0.3-0.6  $\mu$ Sv/h. Actual exposure dose tends to be lower than that is estimated from the air dose rate. (Based on the estimation, annual additional exposure of 1 mSv is converted to air dose rate of 0.23  $\mu$ Sv/h.

### (3) Change of contamination situation


Contamination tends to be topically concentrated under rain gutters etc. in a garden due to weathering and human activities, while it was widespread early on in the incident.

Correlation between the Average Air Dose Rate and the Average Annual Additional Exposure Dose

- Soma City (elementary school pupils) and Date City (0 to 15 years old) -



#### Change of contamination situation



Early on

Present

# For Acceleration of Decontamination and Reconstruction ③ - Interim report of the strategies of the national government and the 4 cities -

### Direction of the future strategies

### (1) Promote radiation protection of the public, focusing on individual exposure dose

- Enhance activities for radiation protection, focusing on individual exposure dose in areas where decontamination was done as planned.
- Promote monitoring of individual doses by providing residents with personal dosimeters.
   (2) Enhance risk communication
- Convey clearly and deliberately the government policy on decontamination, scientific knowledge about radiation, and new findings on effects of decontamination and relationships between air dose rate and individual exposure dose.
- Improve officials' knowledge about decontamination and health impacts of radiation.
- Secure and cultivate human resources who can convey knowledge and ideas of the government and experts.

### (3) Conduct decontamination effectively, depending on the situation of contamination

- Determine whether to conduct decontamination and select appropriate measures, depending on the radiation level.
- Improve effectiveness and efficiency of decontamination activities.


# (4) Enhance comprehensive policies to secure radiation protection and address anxieties of the public

• By effectively combining policies of (1)-(3), address people's concern and retrieve their sense of security.

# Outline

- Policy Framework
- Progress in Special Decontamination Area
- Progress in Intensive Contamination Survey Area
- Decontamination technology
- New policies announced in Sep 2013
- Efforts to secure Interim Storage Facility
- Public Communication

### **Formulation of the Decontamination Guidelines**





- Technical guidelines for carrying out decontamination
- Developed to complement the Ordinance of the Ministry of the Environment
- Used as reference when ordering decontamination projects and the like

#### Contents

- 1. Guidelines on the methods of investigating and measuring the status of environmental pollution in intensive survey areas
- 2. Guidelines pertaining to measures on decontamination and the like
- 3. Guidelines pertaining to the collection and transportation of the removed soil
- 4. Guidelines pertaining to the storage of the removed soil

#### URL:

http://josen.env.go.jp/en/framework/pdf/decontamination\_gui delines\_2nd.pdf

### Techniques Used for Decontamination 1

O Houses, buildings

Removal of deposits from the roof, deck , and gutters Wiping off the roofs and walls, high-pressure washing etc.

- Gardens and standing trees
   Mowing, removal of fallen leaves, topsoil stripping etc.
- O Roads

Removal of deposits in the ditch, high-pressure washing etc.

Decontaminating roofing tiles (by wiping-off)



Decontaminating paved surfaces (by a collective type high-pressure water cleaner)



Decontaminating gardens (by removing soils etc.)



Photos provided by: Date City

### Techniques Used for Decontamination 2

- O Schoolyards, gardens and parks Stripping of soils and topsoil etc.
- O Farmlands Reversal tillage, stripping of topsoil etc.
- O Forests and woods Removal of fallen leaves and lower twigs, pruning etc.

Decontaminating a grass plot



Photo provided by: Japanese Society of Turf grass Science

Decontaminating a schoolyard



Photo provided by: JAEA

Decontaminating a forest (by removing fallen leaves)



Photo provided by: JAEA

### **Summary on Decontamination Effect**

Effect of decontamination works by national and local governments (Major results)

Air dose rate <sup>*1,2</sup> (Measured at 1m height)	Before decontamination: <b>0.36-0.93</b> μSv/h After decontamination: <b>0.25-0.57</b> μSv/h		
Reduction rate (average) of air dose rate <sup>*2,3</sup>	<1µSv/h before decontamination	1-3.8μSv/h before decontamination	> 3.8µSv/h before decontamination
	32%	43%	51%
Example of reduction rate of surface concentration of contamination <sup>*4</sup>	Asphalt-paved roads: 50-70% by washing, 30-70% by high-pressure washing Playground(Soil): 80-90% by stripping off surface-dirt		

\*1: Range from 25 to 75 percentile values of the air dose rate.

\*2: Data measured at 50cm height in children's living environment are not included.

\*3: Average reduction rate of the air dose rate for different dose levels before decontamination.

(Reduction rate (%)= (1-air dose rate after decontamination / air dose rate before decontamination) x100.)

\*4: Already in press release of "Announcement on 'Effectiveness of decontamination work which is implemented by the national government and relevant municipalities in decontamination project' (Jan. 18, 2013)"

#### <Original Data>

OProjects: Mostly, decontamination projects after FY2012

(Projects by national government: 10 municipalities;

Projects by municipalities: 90 municipalities in 8 prefectures)

OData measurement term : Roughly from Mar. 2012 to Oct. 2013

OMeasured item: Air dose rate (measured at 1m and 50cm heights; Unit:  $\mu$ Sv/h)

ONumber of data: About 250,000 (A pair of data collected before and after decontamination is counted as

one item of data)

# Outline

- Policy Framework
- Progress in Special Decontamination Area
- Progress in Intensive Contamination Survey Area
- Decontamination technology
- New policies announced in Sep. 2013
- Efforts to secure Interim Storage Facility
- Public Communication

### **New Policies announced in Sep 2013**

MOE has announced new policies for two items below in September 2013.

### **1. Follow-up policy after decontamination work is completed**

Follow-up policy has newly been established by MOE, according to the completion of decontamination work based on the decontamination plans in several municipalities.

### **2.** Decontamination policy in forest areas

Decontamination in forest area has been limited to within 20 m from the residential area under the current policy. Taking into account voices from Fukushima that hope to widen decontamination target area, decontamination policy for forest areas is also renewed based on relevant results of research.

# Follow up Measures after Completion of Decontamination Work Based on a Plan

#### (Confirmation of maintenance of decontamination effects)

- Conduct relevant monitoring so as to confirm whether air dose reduction by decontamination would be maintained.

#### (Follow-up decontamination work)

- Implement decontamination work in the case of that newly-found contaminated areas(\*) or areas in which un-decontaminated points are found, while considering radiation level there.

(\*) Supposing such area whose air dose rate is higher than that of surrounding area because contaminated soil, etc. is re-accumulated there associated with fallen leaves or rain water and, as a result, air dose rate goes up significantly after the decontamination.

- Require a careful judgment to decide the follow-up decontamination implementation, considering various circumstances of each case. MOE will publish guidance for it by analyzing actual cases.

#### (Others)

- Take relevant measures including risk communication matters based on the ongoing discussion at the Nuclear Emergency Response Headquarters on radiation protection measures.
- In regard with measures on rivers and lakes, monitoring will have been conducted.

### . Measures on forest areas

#### A. Around residential areas

- Make an additional measure possible to remove organic residuals 5m in width from the edge in the case the effects of prior decontamination (by removing organic deposits such as fallen leaves 20m in width) is found to be limited.
- Make an exceptional measure possible to widen the area of decontamination to over 20m in case relatively high air dose rate is monitored around the house even though prior decontamination has been done, supposing such a house located in a valley, etc.

Reflected to "Decontamination Guidelines" (December, 2013)

#### B. Cultivating farm for mushroom

 Make the implementation of standard decontamination method possible, which have been approved around residential areas (20m wide), in a case where cultivating business is expected to be sustained.

De

Described a decontamination method clearly in "Q&A for decontamination" (October, 2013)

#### C. Forest in whole

- Collaborative measures will be conducted by the Ministry of the Environment and the Forestry Agency.

MOE: measures regarding monitoring on runoff and/or diffusion of contaminated soil as well as countermeasures against them

Forestry Agency: measures to take proper forestry management

Implementation planned in FY2014

### (Reference) Related Responses towards Evacuees Returning Home

"The Policy for accelerating Fukushima's reconstruction from the nuclear disaster" (Cabinet Decision, December 20, 2013)

Integrated and multi-tiered protective actions are taken by the related ministries in collaboration with each other. The ministries conduct, or continue to examine, measures of measuring and managing individual doses, reducing radiation exposure in various manners, and establishing a consultation system. With these measures, we continue to pursue the long-term goal (additional individual dose of 1mSv per year or below) for the returned evacuees.

URL; http://www.kantei.go.jp/foreign/96\_abe/actions/201312/20gensiryoku\_e.html

#### "Practical Measures for Evacuees to Return Their Homes" (Nuclear Regulation Authority, November 20, 2013)

One of the practical measures for evacuees to return their home is to focus on the individual dose. For the evacuees to return home, measures that contribute to measure, manage the individual dose, and to reduce radiation exposure of residents are suggested. Also, to establish a system of supporting the evacuees who choose to return home in a comprehensive manner, the necessity of allocating counseling staff and developing a system of supporting them was suggested.

URL; http://www.nsr.go.jp/english/library/data/special-report\_20140204.pdf

# Outline

- Policy Framework
- Progress in Special Decontamination Area
- Progress in Intensive Contamination Survey Area
- Decontamination technology
- New policies announced in Sep 2013
- Efforts to secure Interim Storage Facility
- Public Communication

### What is an Interim Storage Facility (ISF)?

- OIn Fukushima prefecture, large quantities of contaminated soil and waste have been generated from decontamination activities.
- OIt is difficult to clarify methods of final disposal of such soil and waste at the current stage.
- OUntil final disposal becomes available, it is necessary to establish an Interim Storage Facility (ISF) in order to manage and store soil and waste safely and intensively.

The following materials generated in Fukushima prefecture will be stored in the ISF.1. Soil and waste (such as fallen leaves and branches) generated from decontamination activities, which have been stored at the Temporary Storage Sites.



Incineration ash with radioactive concentration more than 100,000 Bq/kg.
 \* In principle, combustible materials will be incinerated, and incinerated ash will be stored.

Note) MOE's policy is that materials such as incinerated ash with radioactive concentration less than 100,000 Bq/kg will be finally disposed at a privately managed disposal site (named Fukushima Eco Tec Clean Center) in Tomioka .

# Process regarding the Interim Storage Facility (1)

Time	Contents		
Oct. 2011	<ul> <li>MOE announced the Basic Principles of the roadmap of the Interim Storage Facility (ISF).</li> <li><b>XMain Contents</b> <ul> <li>The National Government will secure, maintain and manage the ISF</li> <li>The National Government will make utmost efforts to start operating the ISF in about 3 years after start of full-scale collection of soil to the temporary storages sites</li> <li>Only soil and waste generated in Fukushima prefecture will be stored in the ISF</li> <li>The above materials will be finally treated outside Fukushima prefecture within 30 years after launch of interim storage</li> </ul> </li> </ul>		
Mar., 2012	MOE explained the Fukushima prefecture and the 8 towns that the ISF may be located separately in 3 towns (Futaba, Okuma and Naraha).		
Nov., 2012	The Governor of Fukushima announced the acceptance of the investigation proposed by MOE, subject to in-depth explanation to the local communities.		
Apr., 2013-	MOE started the field survey including boring survey, obtaining the consent from the local communities.		
JunSep., 2013	The study groups on safety measures and environmental protection were held.		
Dec., 2013	MOE requested the Fukushima prefecture and the 3 towns (Futaba, Okuma and Naraha) to accept the establishment of the ISF (and also requested Tomioka and Naraha at the same time to utilize the Eco-Tec Clean Center).		
Dec. 2013 — Sep. 2014	MOE reviewed transportation of removed soil, etc. in a study group. 48		


# Process regarding the Interim Storage Facility 2

Time	Contents
Sep. 1, 2014	The Governor accepted the construction of the ISF, and both mayors of Okuma and Futaba conveyed that they took the Governor's acceptance seriously and agreed that the government would explain to the landowners. The Prime Minister Abe met the Governor of Fukushima and the both mayors and the Governor told the Prime Minister the acceptance as well.
The end of Sep. — Oct. 2014	MOE held <u>explanatory meetings for landowners</u> (12 times in total: 9 times in Fukushima and 3 times outside Fukushima).
Oct. — Nov. 2014	In Oct., the amendment bill for the Japan Environmental Safety Corporation (JESCO) Law in order to legislate the final disposal of contaminated soil and waste outside Fukushima prefecture was approved by the Cabinet and submitted to the Diet. <u>The amendment of JESCO Law was enacted in Nov. and implemented in Dec</u>
Nov. – Dec. 2014	MOE finalized the Basic Transportation Plan and proposed a transportation implementation plan in a transportation liaison and coordination meeting consisted of relevant ministries and organizations.
The end of Nov. — Jan. 2015	It announced tender of construction work for stockyard. The contracts were concluded in Jan.
DecJan., 2015	Both Okuma and Futaba accepted the construction of the ISF.

# Process regarding the Interim Storage Facility 3


Time	Contents		
Jan. 16, 2015	MOE confirmed the commencing time of delivery of removed soil to the ISF, announcing if things go according to the plan, it will start the construction of stock yards at the beginning of Feb. and will make every efforts to start the delivery of soil through the pilot-scale transportation before Mar. 11, 2015, if the 5 conditions requested from Fukushima prefecture be fulfilled.		
Jan. 2015	On the basis of transportation liaison and coordination meeting held on 26 <sup>th</sup> , MOE finalized the transportation implementation plan.		
Feb. 3, 2015	The construction of stock yards started.		
Feb. 8, 2015	The Minister of the Environment and the Minister for Reconstruction explained to the Governor of Fukushima the progress related to 5 conditions which should be confirmed before the delivery of soil and waste to the ISF.		
Feb. 25 & 27, 2015	On 25 <sup>th</sup> , the Minister of the Environment and the Minister for Reconstruction had a meeting with the Governor of Fukushima and both mayors of Okuma and Futaba. The Governor and mayors conveyed the acceptance and requested the delivery to be started after Mar. 12, also to pay respect to the residents' visit to their ancestors' graves during the Buddhist season. Based on these requests, the Minister of the Environment announced that MOE will start the delivery from Mar. 13 and will stop the delivery and construction work of the stock yards between Mar. 18 and 24.		
Mar. 13 & 25	MOE started the delivery from a temporary storage site in Okuma and Futaba, respectively.		

### **Planned Site for the Interim Storage Facility**

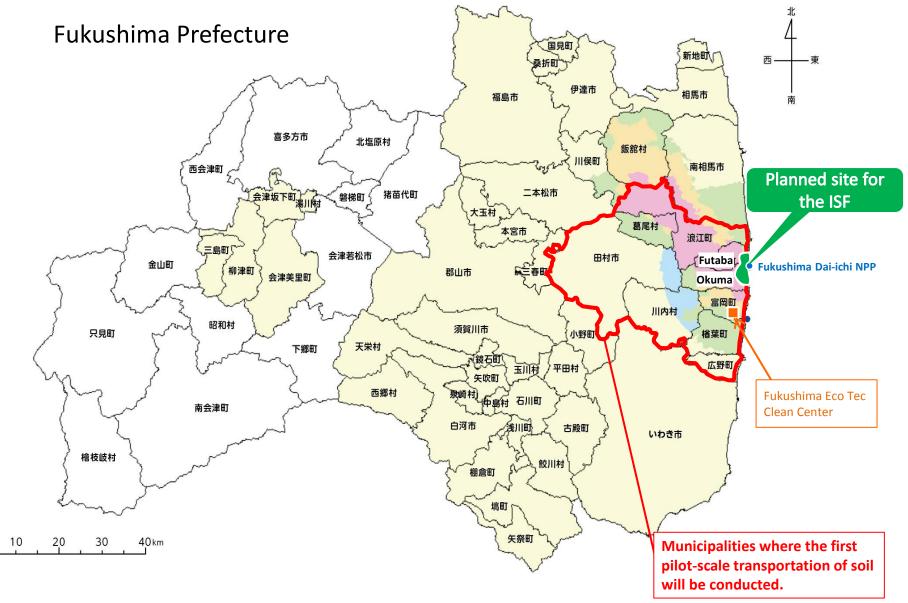


### **Possible Stockpile in the Interim Storage Facility**

(m<sup>3</sup>) Estimated volume of generated soil, etc. from decontamination work (in case of 22 million m<sup>3</sup>)

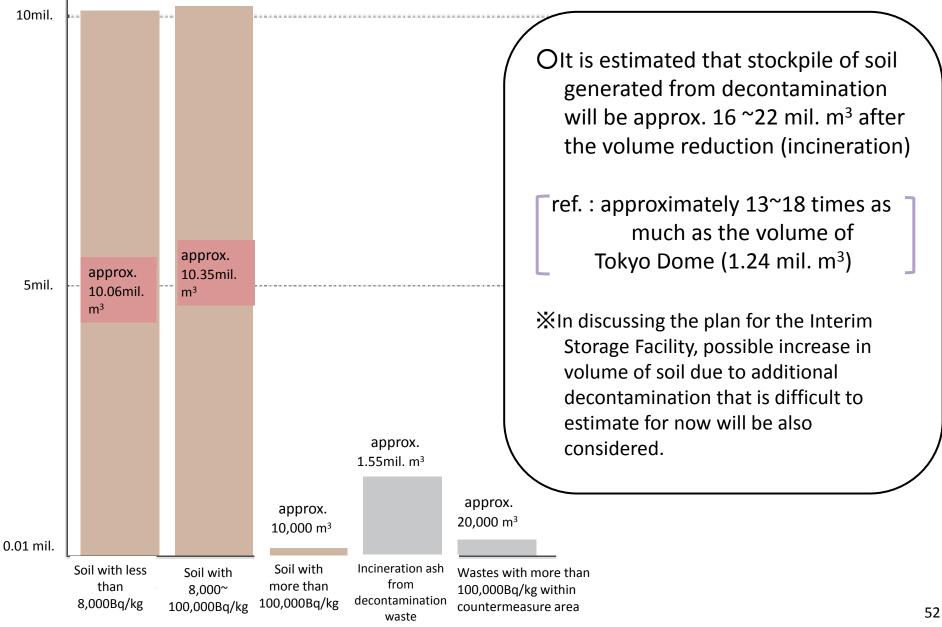

### Layout Drawing of Interim Storage Facilities (draft)

Interim Storage Facility will be consisted of facilities with various functions.
 Those facilities will be developed in accordance with the consent of landowners and the generation of removed contaminated soil, etc.

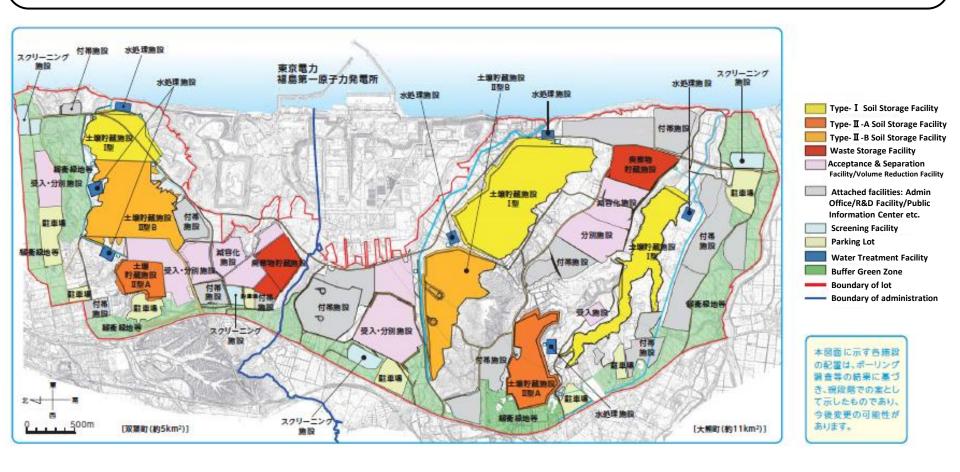

### **Structure Concept on Interim Storage Facility**

< Schematic view of Soil Storage Facility >


Applicable geography and geology: tableland

#### Radioactive cesium concentration: more than 8,000Bq/kg

< Schematic view of waste storage Facility >

Applicable geography and geology: Hill, tableland

Radioactive cesium concentration more than 100,000Bq/kg

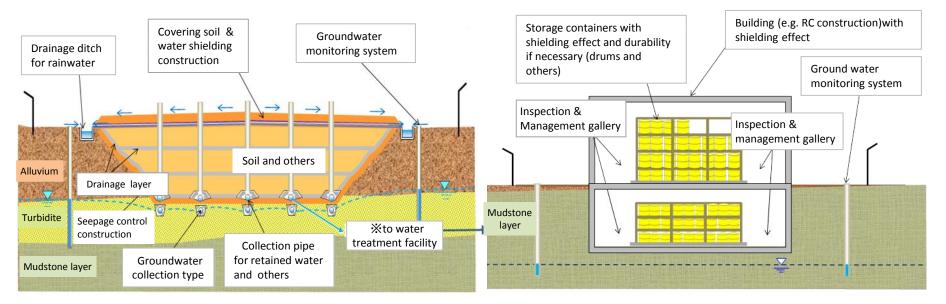

Soil storage facility <Type II B>

XAbove pictures are schematic and details may be reviewed in future, considering geography and geology

### Road Map for Final Disposal outside Fukushima Prefecture

	Start of ISF	30 years from the start of ISF
<b>STEP1:</b> Comprehension of trends in research & development at home and abroad	STEP 1	
<b>STEP2:</b> Studying a direction of future research & development	ST	TEP 2
<b>STEP3:</b> Forwarding research & development		STEP 3
<b>STEP4:</b> Studying a direction of the final disposal considering possibilities of volume reduction and recycling		STEP 4
		Taking soil and waste out of the facility after volume reduction and recycling
<b>STEP5:</b> Investigation, review and adjustment concerning the final disposal site	Development of nation	STEP 5
<b>STEP6</b> : Land preparation of the final disposal site	understanding of fina outside Fukushima	
<b>STEP7:</b> Transfer of soil and waste to the final disposal site		STEP 7
STEP8: Completion of the final disposal		STEP 8

# Outline

- Policy Framework
- Progress in Special Decontamination Area
- Progress in Intensive Contamination Survey Area
- Decontamination technology
- New policies announced in Sep 2013
- Efforts to secure Interim Storage Facility
- Public Communication

## **Public Communication**



🖸 MM-51 🔝 ANAMI-ガイドライン 😳 お校立ちリング第 🎘 サイトマップ 💽 ANN-SDゼ 除染実施区域の概要・進捗
 除染て取り除いた +場応の管理 除込持知道の概要・道法 NOTFILEFER 

6万万川市の没有をとなる、気がなりい、特別市地内地の天向計算を放送していた

検索 文字サイスの変更 小 日 ス

#### 除染特別地域における進捗状況



#### Pamphlets and other materials

- Easy-to-understand and detailed information
- Distributed at meetings, workshops, city offices, banks, convenience stores, etc.
- Available on the Web

#### Newspaper ads and TV programs

Media is the largest information source for people in FP







調べてなっと

**校**康和

#### **Decontamination Information Plaza**

- Information hub of decontamination run by MOE and FP (located near the Fukushima Station)
- Providing people inside and outside of FP and municipalities with comprehensive and latest information of decontamination and radiation

#### Interactive exhibition, demonstration, and workshops



Dispatch of experts to municipalities, communities, schools, etc.

